

#### Alden Central School District

August 8, 2019

# **Board of Education Update**








# Vision 20/20 – Phase 1







# Vision 20/20 – Phase 1

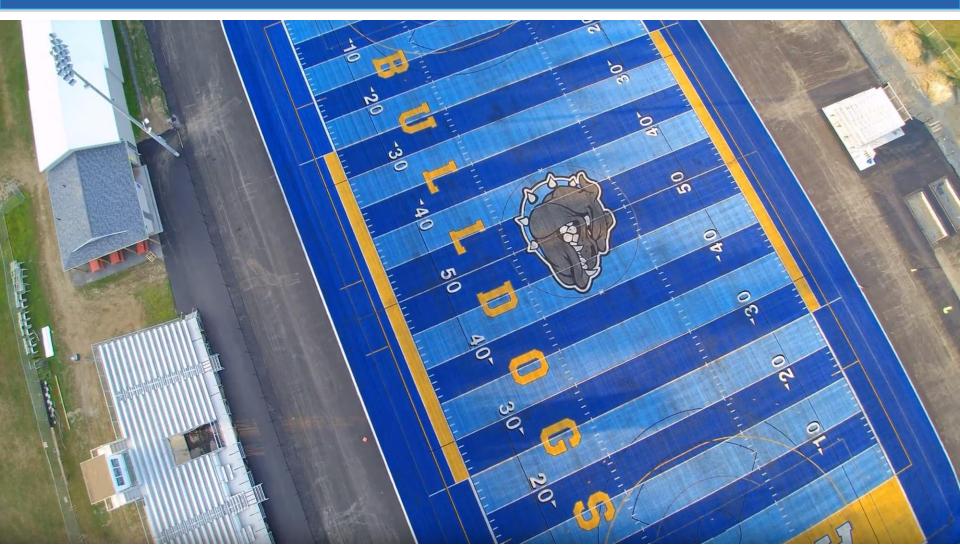





### Vision 20/20 – Aquatic Center







#### Vision 20/20 – Aquatic Center

#### Phase 2 – Summary:

- Bids received on April 5, 2019
- Bid results were over allocated budget
- Presented results to the CBC on April 16<sup>th</sup>
- CBC tasked the group to advise on a course of action – how much money would be needed to move forward with the project







# Vision 20/20 – Aquatic Center Building the Future



### Vision 20/20 – Aquatic Center

#### **Phase 2 – Budget Considerations:**

	Bid Results (with add alternates)	(Overrun)
\$5,539,400	\$10,479,900	(\$4,940,500)

	Re-Bid Budget Estimate
Overrun	\$4,940,500
5% Contingency on Overrun	\$247,025
Increase Contingency to 8%	\$279,080
Escalation (5%)	\$523,995
Additional Incidentals & Reserve	\$320,000
Phase 1 Bid Savings	(\$534,823)
POTENTIAL PROPOSITION	\$5,775,777







#### Alden Central School District

#### SUMMARY OF AVERAGE COST TO TAXPAYER FOR \$100,000 FULL VALUE PROPERTY

			NO STAR
			Non-Primary Residence
	Use of Capital Reserve	Average Annual Local Share	Annual
Scenario 1	\$2,705,000	(\$86)	\$0
Scenario 2	\$2,500,000	\$19,301	\$2
Scenario 3	\$2,250,000	\$42,359	\$4
Scenario 4	\$2,000,000	\$65,257	\$7
Scenario 5	\$1,750,000	\$88,374	\$9

Note: Abstracted from full Projected Financial Impact Scenario Reports

cjd/nsb Updated: 8/7/2019 Printed: 8/8/2019

#### Vision 20/20

#### **Next Steps and Potential Future Schedule:**

- August 8th Board of Education determines to move forward with a new resolution.
- October Vote
- November/December 2019 Re-bid project
- Construction Starting spring/summer 2020





# Questions

